


PHASE 2:
 Anticipated construction start date for Assessment District No. 124 - Phase 2 is late 2024/early 2025. The construction contract for this project was awarded in November 2024.

LEGEND

| | | | |
|--|---|--|--------------------------------------|
| | PHASE 1: 02/12/24 - 03/14/24 | | PHASE 10: 09/06/24 - 10/04/24 |
| | PHASE 2: 03/15/24 - 04/04/24 | | PHASE 11: 10/04/24 - 10/29/24 |
| | PHASE 3: 03/29/24 - 04/30/24 | | PHASE 12: 10/28/24 - 11/13/24 |
| | PHASE 4: 04/26/24 - 05/29/24 | | PHASE 13: 11/14/24 - 12/13/24 |
| | PHASE 5: 05/20/24 - 06/17/24 | | PHASE 14: 12/09/24 - 01/14/25 |
| | PHASE 6: 06/10/24 - 06/25/24 | | PHASE 15: 01/06/25 - 02/14/25 |
| | PHASE 7: 06/24/24 - 07/09/24 (NO WORK 7/4 - 7/5) | | PHASE 16: 01/27/25 - 03/04/25 |
| | PHASE 8: 07/09/24 - 08/16/24 | | PHASE 17: ON HOLD |
| | PHASE 9: 08/20/24 - 09/12/24 | | ASSESSMENT DISTRICT AREA BOUNDARY |
| | COMPLETED WORK | | |

**PHASING PLAN SUBJECT TO CHANGE

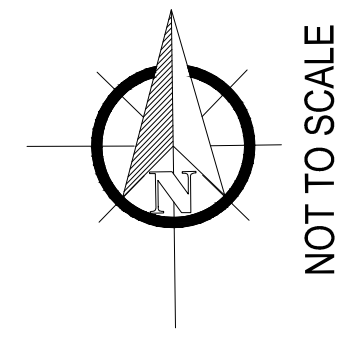

**UNDERGROUND UTILITY ASSESSMENT DISTRICT
 NO. 124 (CENTRAL BALBOA ISLAND - PHASE 1)
 PHASING PLAN**

**CITY OF NEWPORT BEACH
 PUBLIC WORKS DEPARTMENT
 C-9451-1
 12/18/24**
