


**PHASE 2:**  
 Anticipated construction start date for Assessment District No. 124 - Phase 2 is late 2024/early 2025. The construction contract for this project was awarded in November 2024.

**LEGEND**

	PHASE 1: 02/12/24 - 03/14/24		PHASE 10: 09/06/24 - 10/04/24
	PHASE 2: 03/15/24 - 04/04/24		PHASE 11: 10/04/24 - 10/29/24
	PHASE 3: 03/29/24 - 04/30/24		PHASE 12: 10/28/24 - 11/13/24
	PHASE 4: 04/26/24 - 05/29/24		PHASE 13: 11/14/24 - 12/13/24
	PHASE 5: 05/20/24 - 06/17/24		PHASE 14: 12/09/24 - 01/14/25
	PHASE 6: 06/10/24 - 06/25/24		PHASE 15: 01/06/25 - 02/14/25
	PHASE 7: 06/24/24 - 07/09/24 (NO WORK 7/4 - 7/5)		PHASE 16: 01/27/25 - 03/11/25
	PHASE 8: 07/09/24 - 08/16/24		PHASE 17: ON HOLD
	PHASE 9: 08/20/24 - 09/12/24		ASSESSMENT DISTRICT AREA BOUNDARY
			COMPLETED WORK

\*\*PHASING PLAN SUBJECT TO CHANGE

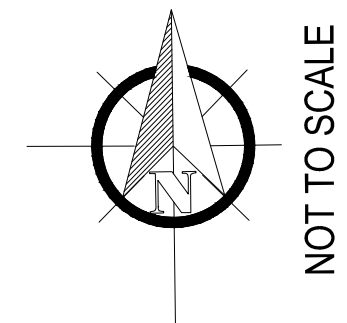

**UNDERGROUND UTILITY ASSESSMENT DISTRICT  
 NO. 124 (CENTRAL BALBOA ISLAND - PHASE 1)  
 PHASING PLAN**

**CITY OF NEWPORT BEACH  
 PUBLIC WORKS DEPARTMENT  
 C-9451-1      01/22/25**
