


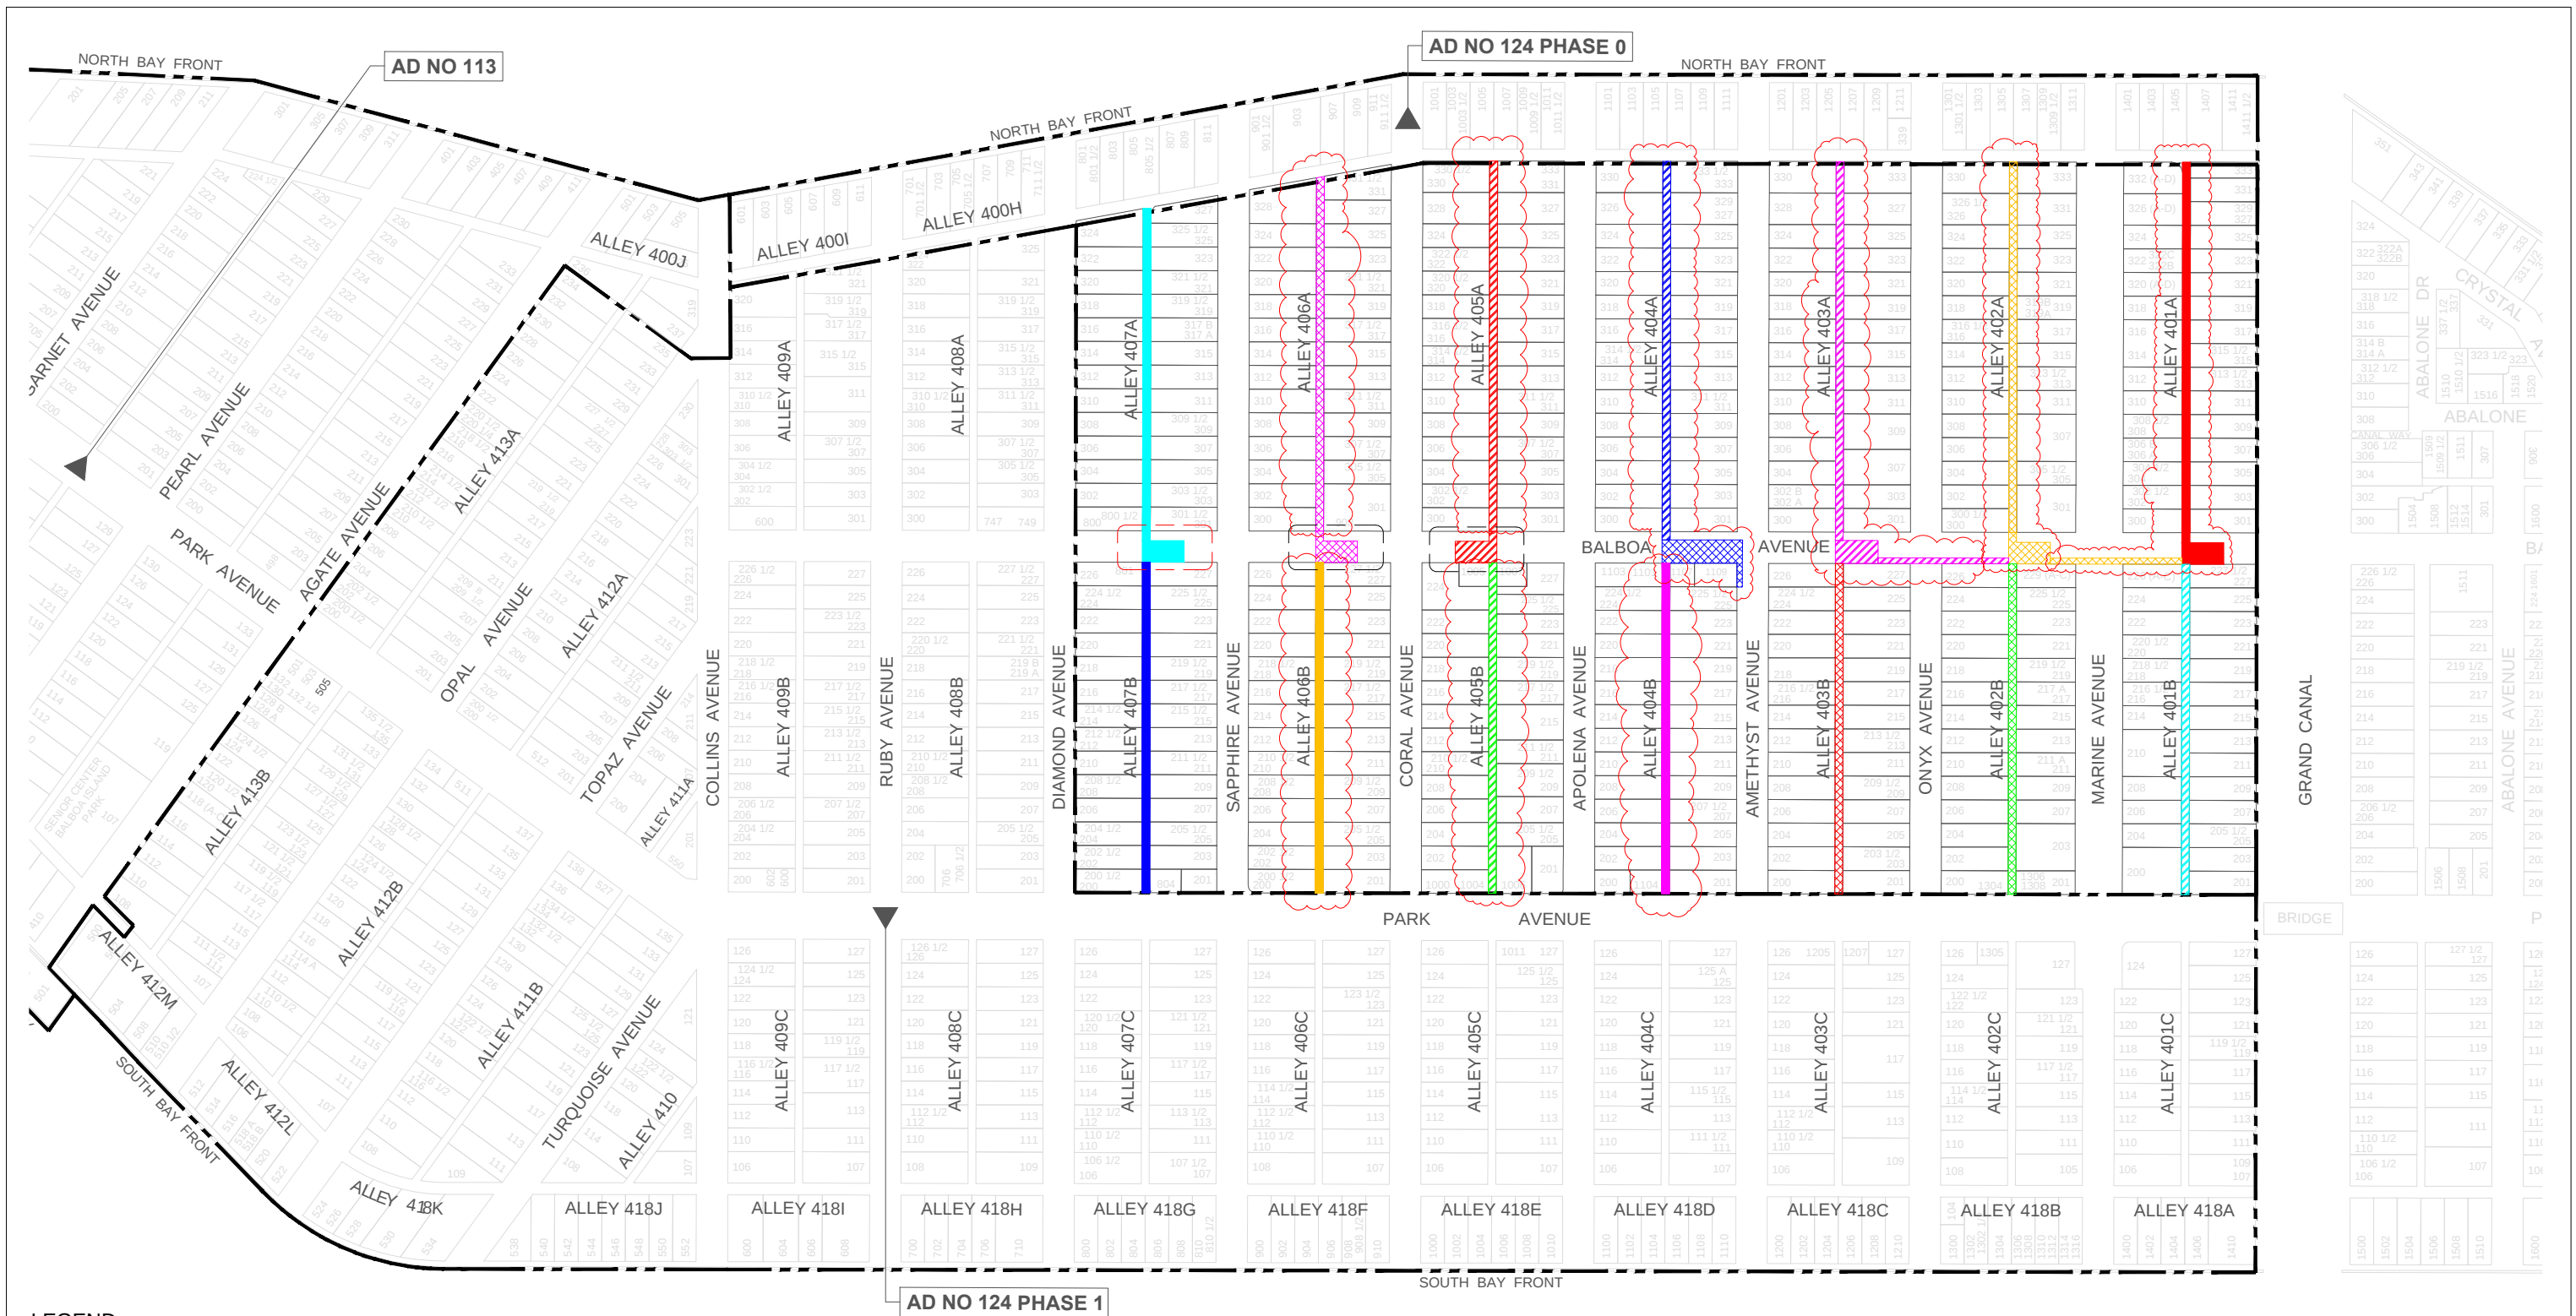

LEGEND

- PHASE 1: 02/03/25 - 03/21/25
- PHASE 2: 03/24/25 - 05/02/25
- PHASE 3: 04/14/25 - 05/23/25
- PHASE 4: 04/23/25 - 05/16/25
- PHASE 5: 05/05/25 - 06/20/25
- PHASE 6: 05/05/25 - 06/20/25
- PHASE 7: 06/23/25 - 07/30/25
- PHASE 8: 06/23/25 - 07/30/25
- PHASE 9: 07/28/25 - 09/05/25
- PHASE 10: 07/28/25 - 09/05/25
- PHASE 11: 09/04/25 - 10/24/25
- PHASE 12: 09/08/25 - 10/24/25
- PHASE 13: 10/27/25 - 12/19/25
- PHASE 14: 11/10/25 - 12/16/25
- PHASE 15: 11/03/25 - 12/09/25
- ASSESSMENT DISTRICT AREA BOUNDARY
- COMPLETED WORK

VAULT WORK

 10/27/25 - 11/14/25

VAULT WORK

 11/17/25 - 12/22/25

UNDERGROUND UTILITY ASSESSMENT DISTRICT
NO. 124 (CENTRAL BALBOA ISLAND - PHASE 2)

PHASING PLAN

CITY OF NEWPORT BEACH
PUBLIC WORKS DEPARTMENT

C-9451-2

09/22/25

**PHASING PLAN SUBJECT TO CHANGE
